

PMO GOVERNANCE FRAMEWORK

Onboarding Solace Health onto the Brightloop Platform

A simulated multi-workstream client onboarding, run under a formal PMO governance model

Folashekemi Vanessa Joshua

PMO Lead / Onboarding Project Manager

Simulated / not real client work

The scenario

Brightloop is a fictional B2B SaaS company providing care-coordination software to healthcare provider networks. **Solace Health**, a fictional 12-clinic healthcare network, has signed on as a new client.

Four workstreams had to land together inside 8 weeks technical integration, data migration, staff training and legal sign-off, so the engagement was run under a formal PMO governance model rather than a single flat project plan, with me as PMO Lead.

NOTE

This is a simulated practice project applying a PMO governance framework to a multi-workstream client onboarding, built to demonstrate PMO and project coordination skills. The companies and figures are fictional.

Project brief

Client	Solace Health — fictional 12-clinic healthcare network
Project	Platform onboarding & go-live across all 12 clinics
Objective	Go-live in 8 weeks with zero critical defects, 2 years of records migrated, all staff trained and BAA/DPA signed
Duration	8-week onboarding, plus a 2-week hypercare period
Sponsors	Brightloop VP of Customer Success & Solace Health COO
PMO Lead	Folashekemi Vanessa Joshua (simulated role)
Governance model	Steering Committee + Working Group + stage-gate reviews
Workstreams	Technical Integration, Data Migration, Training & Enablement, Legal & Compliance

Scope & boundaries

IN SCOPE

- Platform configuration & SSO for all 12 clinics
- Migration of 2 years of scheduling & records data
- 3 role-based training tracks (front-desk, clinician, admin)
- BAA, DPA & security questionnaire sign-off
- Cutover to go-live & a 2-week hypercare period

OUT OF SCOPE

- Custom integrations beyond the standard API
- Replacing Solace Health's existing EHR system
- Post-hypercare optimisation work (phase 2)
- New clinic sites added after kickoff

Governance structure

Steering Committee

Brightloop VP Customer Success, Solace Health COO, PMO Lead

Biweekly: scope, budget & timeline
escalations, go-live decision



Working Group

4 Workstream Leads + PMO Lead

Weekly: RAG review, cross-workstream
dependencies, risks & issues



Workstream teams

Individual contributors on each of the 4 workstreams

Daily : task execution & async
check-ins

The four workstreams

Technical Integration

SSO, API configuration & network setup across all 12 clinics

Lead: Solutions Engineer (Efe)

Data Migration

Extract, cleanse & load 2 years of scheduling and records data

Lead: Data Engineer (Priya)

Training & Enablement

3 role-based tracks — front-desk, clinician, admin, with train-the-trainer

Lead: Customer Success Manager (Marcus)

Legal & Compliance

BAA, DPA and security questionnaire sign-off


Lead: Legal Counsel (Grace)

RACI — key decisions & deliverables

Deliverable	PMO Lead	Brightloop Sponsor	Solace COO	Workstream Leads	Legal Counsel
Charter & kickoff sign-off	R	A	A	C	I
Data migration plan approval	A	I	C	R	I
Security questionnaire & BAA sign-off	C	I	I	C	R/A
Training schedule & materials approval	A	I	I	R	I
UAT sign-off	C	I	A	R	I
Go-live readiness decision	C	A	A	C	I
Hypercare exit / project closure	A	I	C	R	I

R = Responsible · A = Accountable · C = Consulted · I = Informed

Onboarding plan: 8 weeks + hypercare

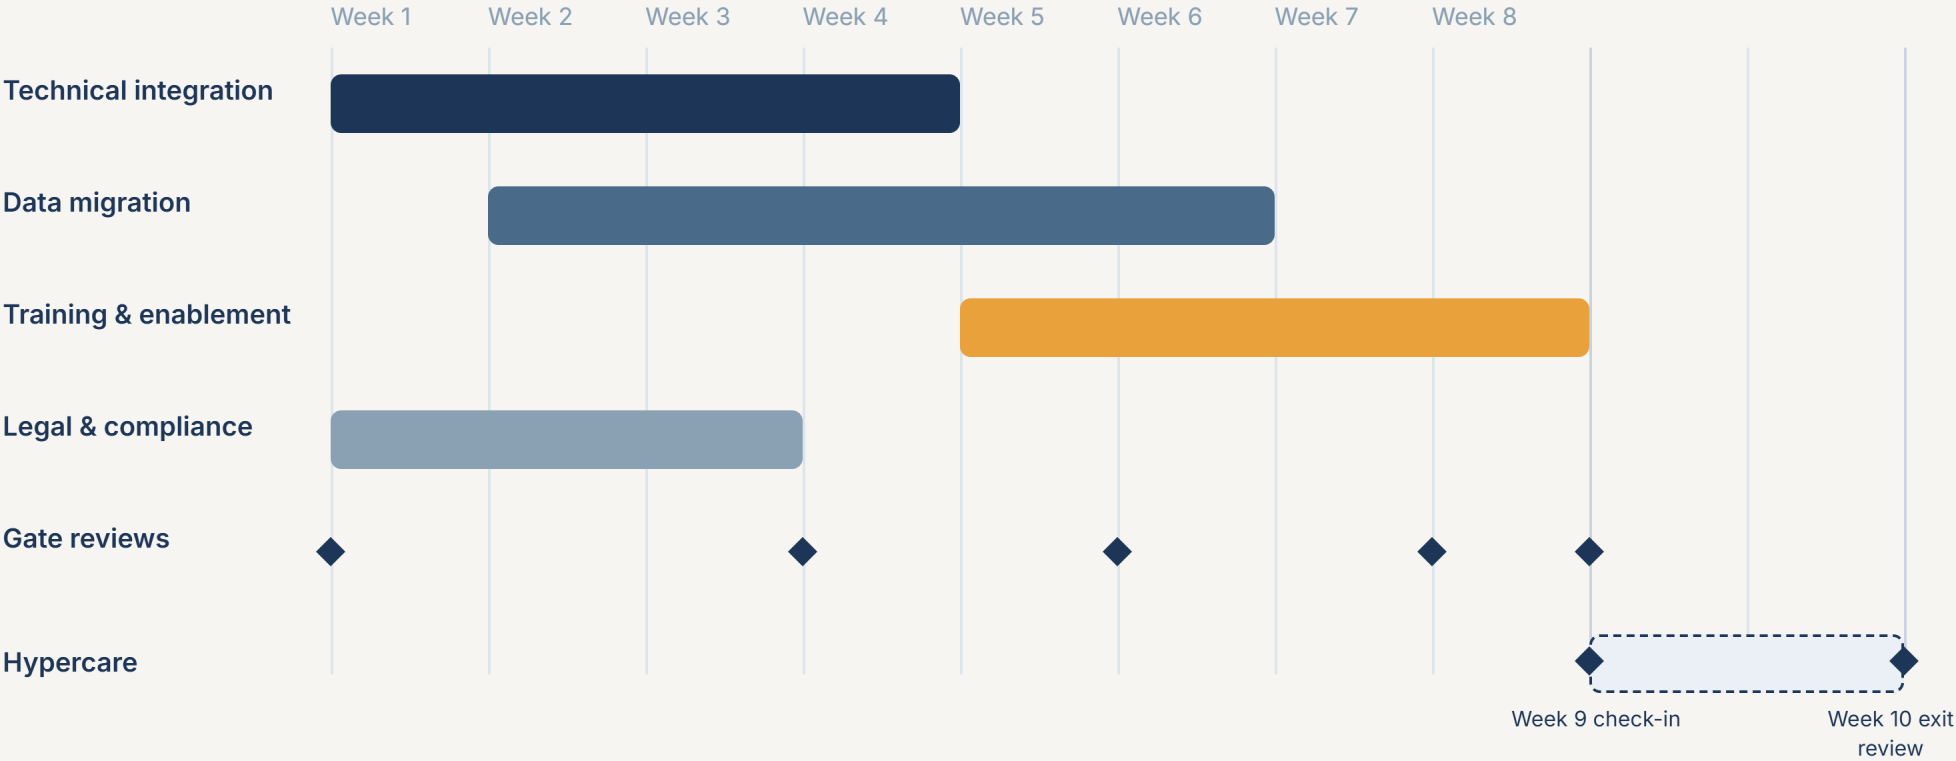

Diamonds mark stage-gate reviews: Kickoff, Design, Build, Test/UAT and Go-live see the Gate Reviews slide for pass criteria.

Governance cadence

Meeting	Frequency	Attendees	Purpose
Daily standup	Daily	Workstream teams	15-minute async task check-in per workstream
Weekly status meeting	Weekly	Working Group	RAG review, cross-workstream dependencies, risk & issue resolution
Steering Committee	Biweekly	Sponsors + PMO Lead	Decisions, escalations, scope/budget/timeline changes
Change control review	Ad hoc	PMO Lead + affected leads	Assess and route any change request against the baseline
Stage-gate review	At each gate	Steering Committee	Go / no-go decision against that gate's exit criteria

Week 5 status report: Working Group

Overall: AMBER


- **Technical Integration** SSO configured and tested across all 12 clinics; on track
- **Data Migration** Legacy data cleansing 3 days behind; catch-up plan agreed with vendor
- **Training & Enablement** Train-the-trainer complete for all 3 tracks; on schedule
- **Legal & Compliance** BAA still pending Solace Health legal signature; escalated to Steering Committee

Next steps: PMO to follow up directly with Solace Health legal counsel before Wednesday's steering committee

RAID log

Type	Description	Owner	Status
Risk	Legacy scheduling data has inconsistent clinic ID formats across sites	Data Engineer (Priya)	Open: mapping table built before migration
Issue	Solace Health legal delayed returning the signed BAA past the week 3 target	PMO Lead	Open :escalated to Steering Committee
Dependency	Go-live gate depends on UAT sign-off from all 12 clinic leads	PMO Lead	On track
Assumption	Solace Health provides one point of contact per clinic for training scheduling	Customer Success Manager (Marcus)	Confirmed at kickoff

Change control process



Urgent changes can be fast-tracked to an ad hoc Steering Committee review rather than waiting for the biweekly cycle

Stakeholder register

Stakeholder	Organisation	Interest / influence	Engagement approach
VP Customer Success (Sponsor)	Brightloop	High / High	Biweekly steering updates, primary escalation point
COO (Executive Sponsor)	Solace Health	High / High	Biweekly steering updates, go-live sign-off
4 Workstream Leads	Brightloop	High / Medium	Weekly Working Group, daily standups
12 Clinic Managers	Solace Health	Medium / Medium	Training schedule updates, UAT participation
Legal Counsel	Solace Health	Medium / High (blocking)	Direct PMO follow-up, escalation as needed
Front-desk & clinical staff	Solace Health	Low / Low	Training sessions, go-live communications

Stage-gate reviews

Gate	Exit criteria	Outcome
Kickoff (Wk 1)	Charter signed, governance model agreed, leads assigned	Passed
Design (Wk 2)	Technical integration design and data migration plan approved	Passed
Build (Wk 4)	Platform configured for all 12 clinics, migration environment ready	Passed with conditions
Test / UAT (Wk 7)	UAT sign-off from clinic leads, security questionnaire closed	Passed
Go-Live (Wk 8)	Steering Committee go/no-go decision, cutover plan confirmed	Passed — go-live approved
Hypercare Exit (Wk 10)	No open critical/high issues, support handed to BAU team	Passed

Tools used

Jira

Workstream task tracking across all four teams

Confluence

Charter, governance model and project documentation

Smartsheet

RAID log and weekly status reporting

Microsoft Teams

Steering Committee, Working Group and daily standups

DocuSign

BAA, DPA and contract sign-off

Power BI

RAG status dashboard for the Steering Committee

Final result & retrospective

WHAT WORKED

- All 12 clinics went live on schedule in week 8 with zero critical defects
- Stage-gate reviews caught the legal delay early enough to escalate before it threatened go-live
- RAG status reporting kept the Steering Committee focused only on the amber/red items

WHAT I'D IMPROVE

- Start the legal & compliance workstream 1–2 weeks earlier, given its history of slow turnaround
- Build a shared clinic-level tracker so 12 individual UAT sign-offs don't bottleneck in the final week
- Add a dedicated change-control log review to every Working Group meeting, not just ad hoc
