

SCRUM-MANAGED CAMPAIGN

Launching Verdae's Calm Barrier Serum in Two Sprints

A simulated 4-week product launch campaign, run as Scrum, for a fictional skincare brand

Folashekemi Vanessa Joshua

Scrum Master & Campaign Lead

Simulated / not real client work

The scenario

Verdae is a fictional independent skincare brand launching its first barrier-repair product, the **Calm Barrier Serum**, for customers with sensitive skin.

The founder wanted a tight, visible launch plan rather than an open-ended marketing push, a natural fit for running the campaign as two two-week sprints, with me as Scrum Master.

NOTE

This is a simulated practice project applying Scrum to a marketing campaign, built to demonstrate Scrum Master and campaign coordination skills. The brand and figures are fictional.

Project brief

Client	Verdae (fictional independent skincare brand)
Project	Product launch campaign for the Calm Barrier Serum
Objective	Build a 5,000-person waitlist before launch and convert 1,200 pre-orders in the first two weeks
Duration	4 weeks, run as two 2-week sprints
Sponsor	Verdae Founder
Scrum Master & Campaign Lead	Folashekemi Vanessa Joshua (simulated role)
Methodology	Scrum — two 2-week sprints with sprint planning, daily check-ins, review and retro
Team involved	Founder, Designer, Copywriter, Paid Social Specialist, 3 micro-influencers (external)

Scope & deliverables

- Landing page with a waitlist sign-up form
- 15-second teaser video and a 6-post social content calendar
- Three-email launch sequence: teaser, launch day, cart reminder
- Three micro-influencer partnerships with briefed content
- Launch-day paid ad set across Instagram and TikTok
- End-of-campaign performance report

Campaign plan — 4 weeks



Campaign backlog

Backlog item	Points	Priority	Sprint
Landing page with waitlist form	8	High	1
Teaser video (15s)	5	High	1
Social content calendar (6 posts)	5	High	1 & 2
Influencer briefing & 3 partnerships	8	Medium	1 & 2
3-email launch sequence	5	High	1 & 2
Launch-day paid ad set	5	High	2
End-of-campaign performance report	3	Medium	2

Two sprints, one launch

SPRINT 1 · WEEKS 1–2

Build awareness

Sprint goal: grow the waitlist to 5,000 before launch day

20 points committed

SPRINT 2 · WEEKS 3–4

Launch & convert

Sprint goal: hit 1,200 pre-orders in the first two weeks of launch

18 points committed

Sprint 1 board: day 6 snapshot

TO DO

Send email 1 teaser

2 pts

IN PROGRESS

Social calendar 3 of 6 posts drafted

5 pts

**Influencer briefing sent,
awaiting confirmations**

2 pts

DONE


Landing page & waitlist form live

8 pts

Teaser video shot & edited

5 pts

Sprint 1 burndown

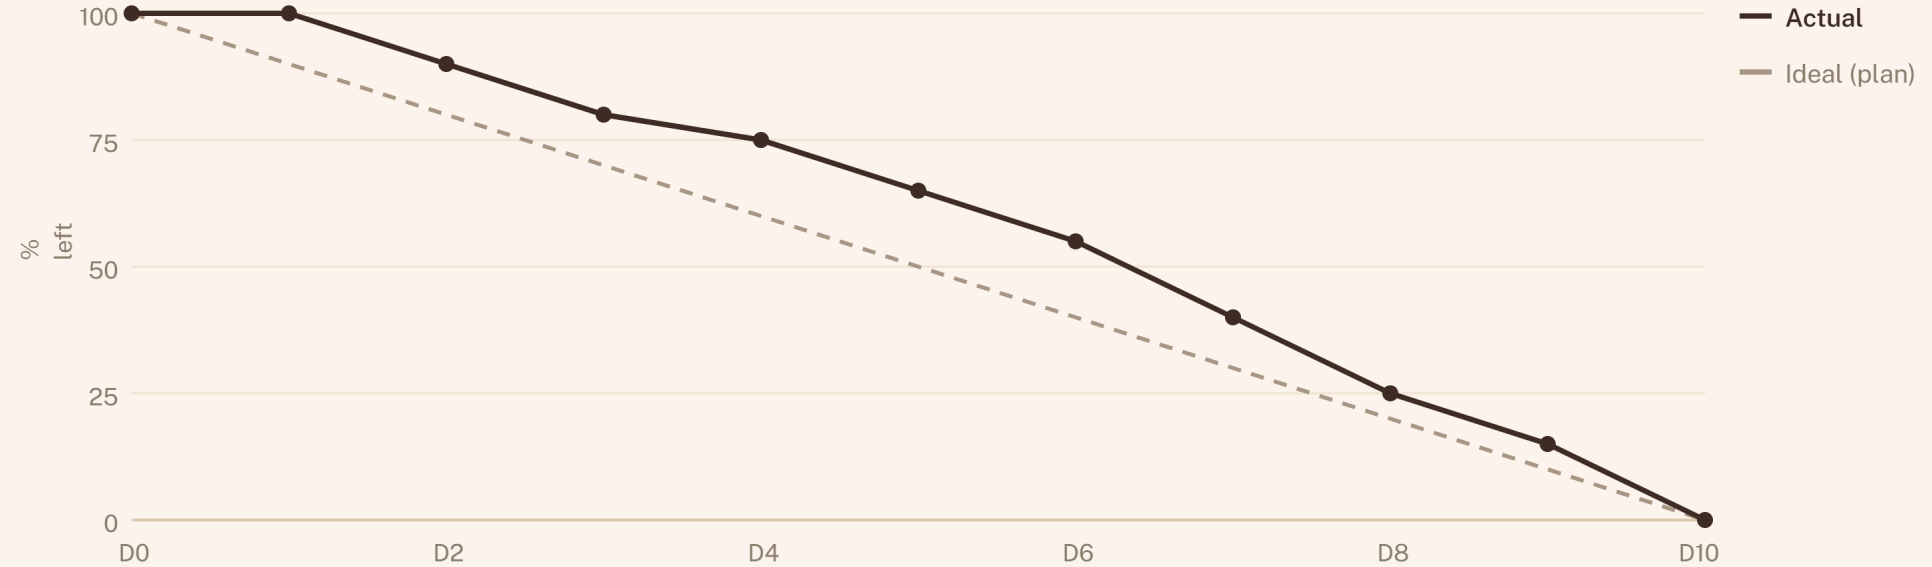

Sprint scope: 20 points. The team ran slightly behind through day 4, then caught up after re-prioritising the social calendar on day 5.

Sprint 1 review & retro

WENT WELL

- Landing page and teaser video both shipped on the first attempt, no rework
- Waitlist hit 4,600 signups by day 10, close to the 5,000 target
- Influencer briefing went out early, giving partners more lead time

DIDN'T GO WELL

- Social content calendar slipped only 3 of 6 posts drafted by day 6
- Underestimated how long influencer contract sign-off would take

CHANGE FOR SPRINT 2

- Split the social calendar into smaller daily tasks instead of one big item
- Start influencer contracts a day earlier next time
- Add a daily 10-minute stand-up to catch slippage sooner

Content approval process



Same-day turnaround target: 24 hours from draft to sign-off, to keep pace with the sprint cadence

Sprint 2 board: day 5 snapshot

TO DO

Performance report draft

3 pts

IN PROGRESS

Launch-day paid ad set creative in review

5 pts

Cart reminder email and copy drafted

2 pts

DONE

All 3 influencer posts live

6 pts


Remaining 3 social posts published

3 pts

Launch email sent

2 pts

Sprint 2 burndown

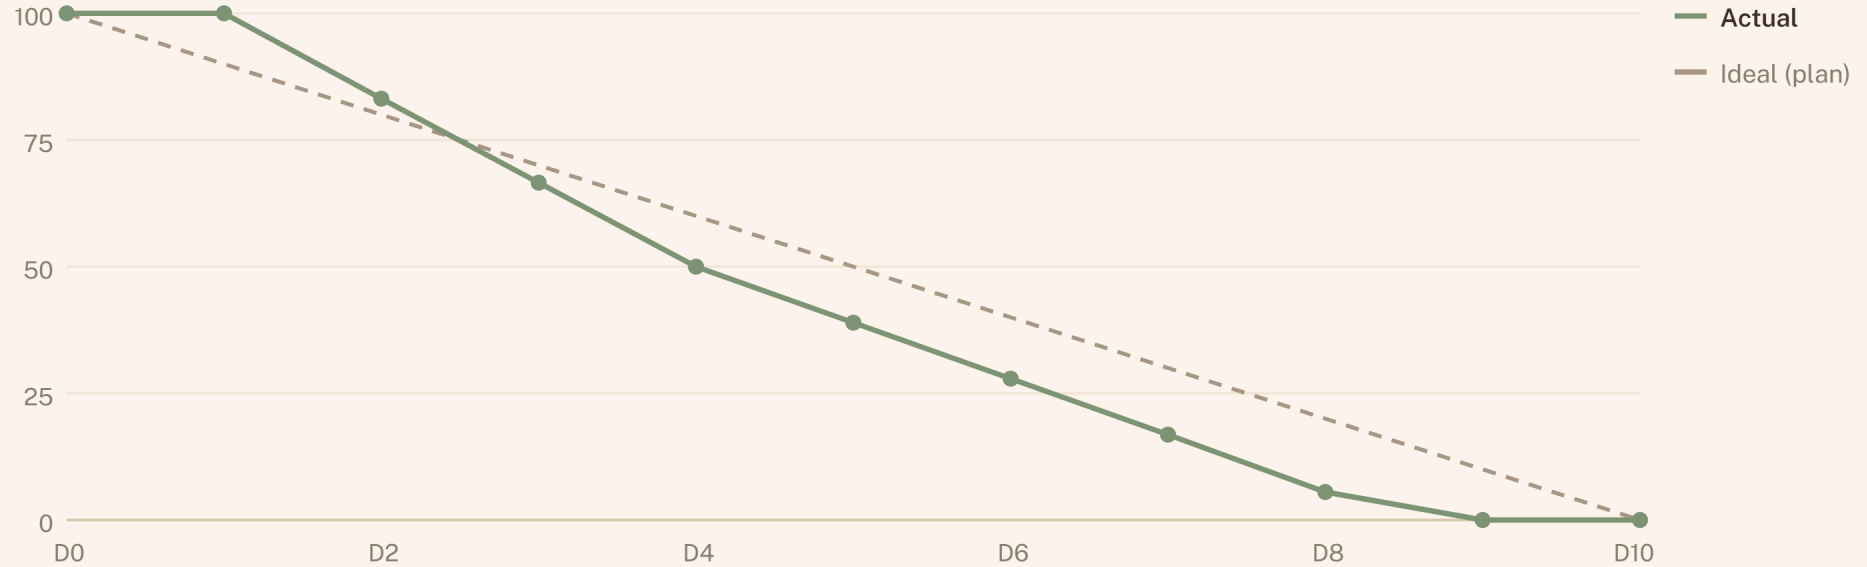

Sprint scope: 18 points. The team cleared the backlog a day early, having tightened estimates after Sprint 1's retro.

Sprint 2 review & retro

WENT WELL

- Splitting the social calendar into daily tasks fixed Sprint 1's biggest slip
- All 3 influencer partnerships live on time, driving a launch-day traffic spike
- Team cleared the sprint backlog a day early

DIDN'T GO WELL

- Paid ad creative needed a same-day revision after the first review
- Cart reminder email went out a few hours later than planned

CARRIED FORWARD

- Build in a same-day creative review buffer for future paid campaigns
- Pre-schedule time-sensitive emails a full day ahead, not same-day

Scrum Master reflections

Ceremony	Facilitation notes
Sprint planning	Timeboxed to 45 minutes; had the team estimate in points before I revealed the sprint goal, to avoid anchoring
Daily check-in	Added from Sprint 2 onward a 10-minute a sync Slack update rather than a live call, to fit a small team's schedule
Sprint review	Walked the Founder through the live board rather than a separate slide deck — kept it to what shipped and what didn't
Retrospective	Used a simple "went well / didn't / change" format; made sure the one process change actually got carried into the next sprint plan
Impediment removed	Influencer contract delay in Sprint 1 escalated to the Founder directly rather than letting it sit in the backlog

End-of-campaign report

Metric	Target	Actual
Waitlist signups (pre-launch)	5,000	5,380
Pre-orders (first 2 weeks)	1,200	1,340
Influencer-driven traffic (launch day)	—	31% of sessions
Email open rate (launch email)	28%	34%
Sprint scope delivered on time	100%	100%

Figures are illustrative targets and results set for this simulated project, not real brand data

Tools used

Trello

Sprint board — To do / In progress / Done, one board per sprint

Canva

Social posts, teaser video captions and the landing page mockup

Meta Ads Manager

Launch-day paid ad set across Instagram and TikTok

Mailchimp

The 3-email launch sequence and waitlist confirmation flow

Google Analytics

Tracking waitlist conversions and influencer-driven traffic

Slack

Async daily check-ins and influencer coordination

Final result & retrospective

WHAT WORKED

- Both sprints delivered their full committed scope on time
- Waitlist and pre-order targets both beaten (5,380 vs. 5,000; 1,340 vs. 1,200)
- The Sprint 1 retro's fix, breaking the social calendar into daily tasks visibly improved Sprint 2's pace

WHAT I'D IMPROVE

- Start influencer contracting in a "Sprint 0" before the campaign clock starts
- Build a same-day creative-review buffer into paid ad tasks from the start
- Track a leading indicator (daily waitlist growth) during Sprint 1, not just the sprint-end total
